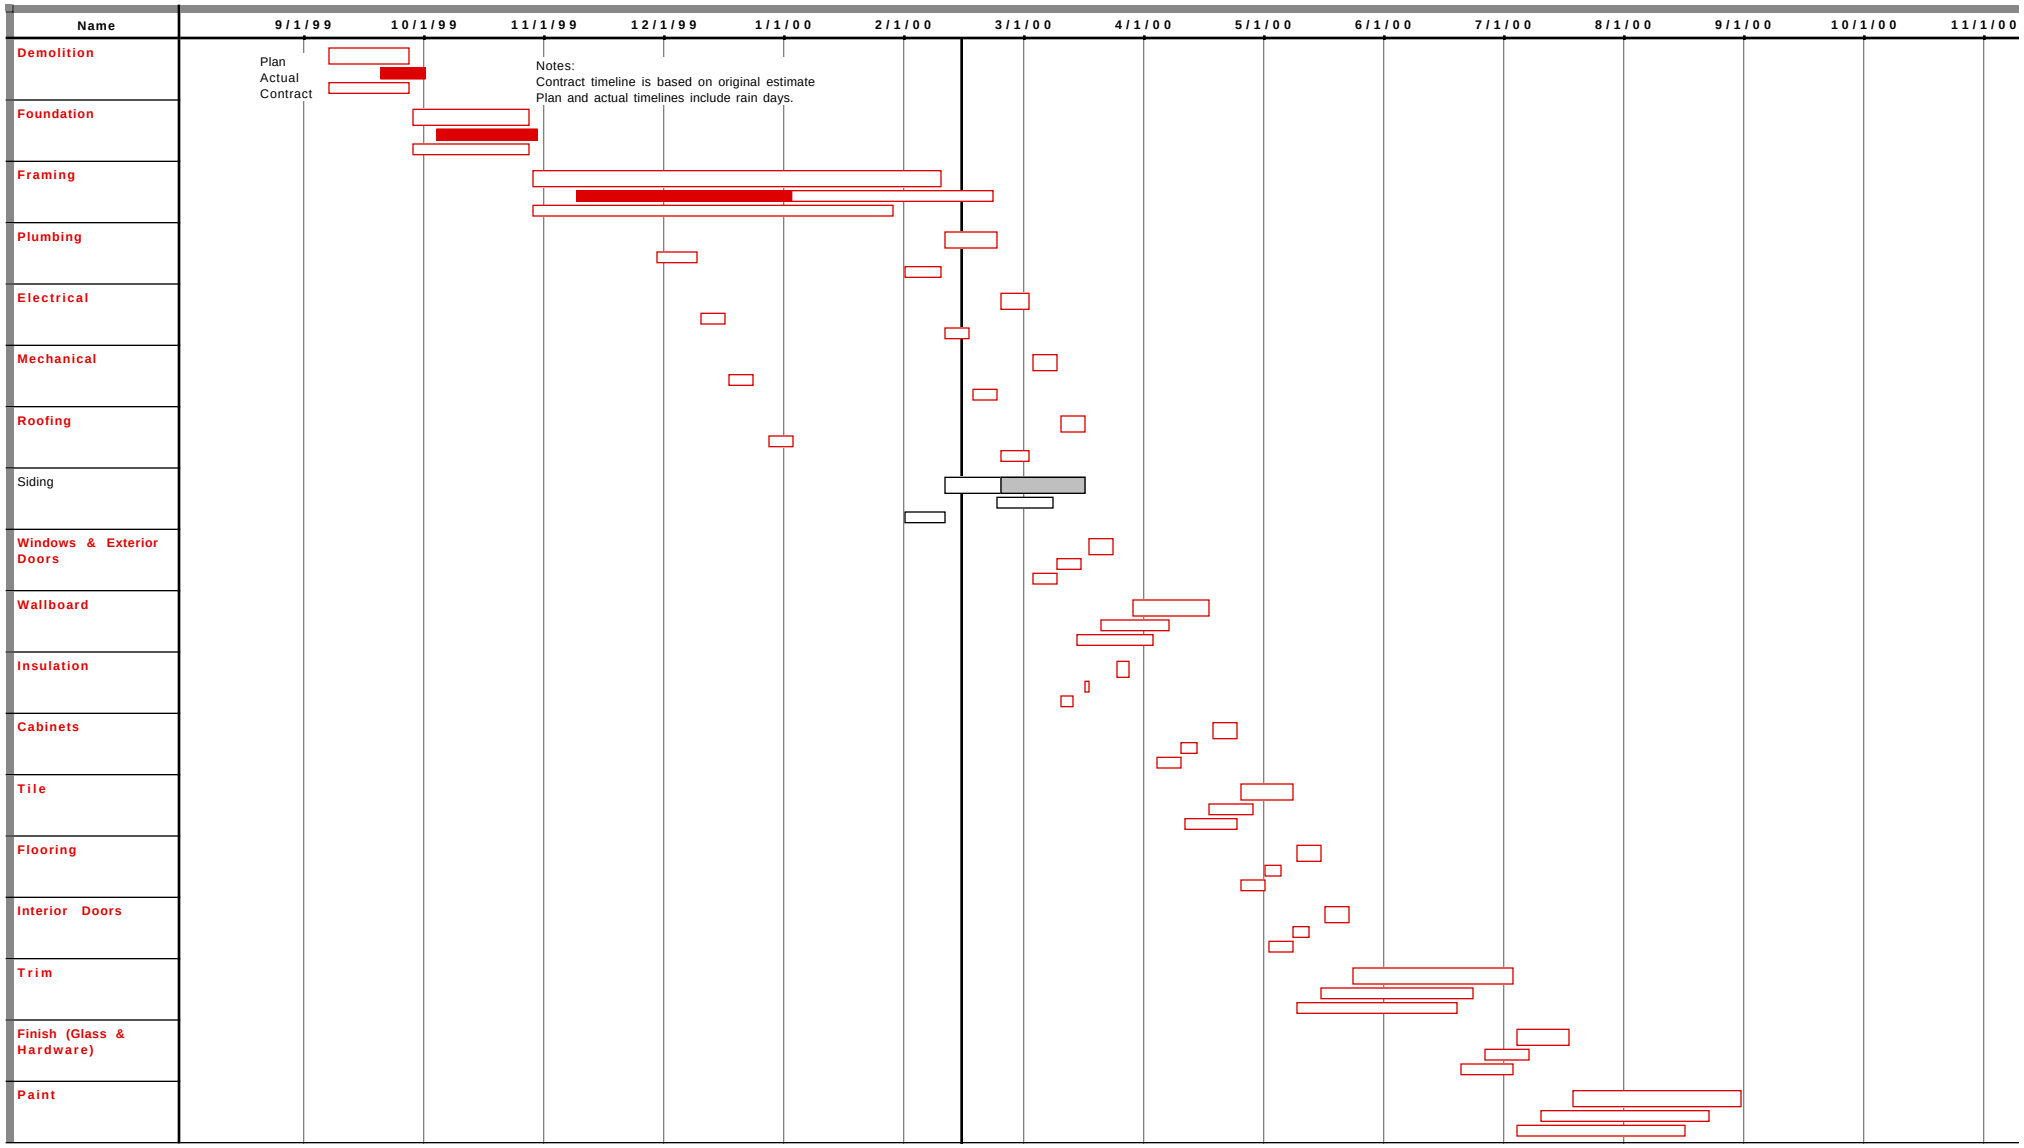
Name
9/1/99
10/1/99
11/1/99
12/1/99
1/1/00
2/1/00
3/1/00
4/1/00
5/1/00
6/1/00
7/1/00
8/1/00
9/1/00
10/1/00
11/1/00
Demolition
Foundation
Framing
Plumbing
Electrical
Mechanical
Roofing
Siding
Windows & Exterior Doors
Wallboard
Insulation
Cabinets
Tile
Flooring
Interior Doors
Trim
Finish (Glass & Hardware)
Paint
Plan
Actual
Contract
Notes:
Contract timeline is based on original estimate
Plan and actual timelines include rain days.
